



Meeting Agenda  
Illinois Department of Transportation Kickoff Meeting  
Wolf Road Reconstruction Phase I  
Section No. 20-00014-00-PV


Virtual Meeting  
November 24, 2020, 1:30 P.M.

Invited

---

John DuRocher	Matt Gazdziak	Moe Kawash	Tara Orbon
Mike Fricano	Tom Hinshaw	Shawn Kennedy	
Darcie Gabrisko	Sanjay Joshi	Marilyn Solomon	

1. Introductions
2. Project Overview
3. Project Funding
4. Public Involvement
5. Anticipated Schedule
  - a) Tasks Completed to Date
  - b) Upcoming Tasks
6. Open Forum

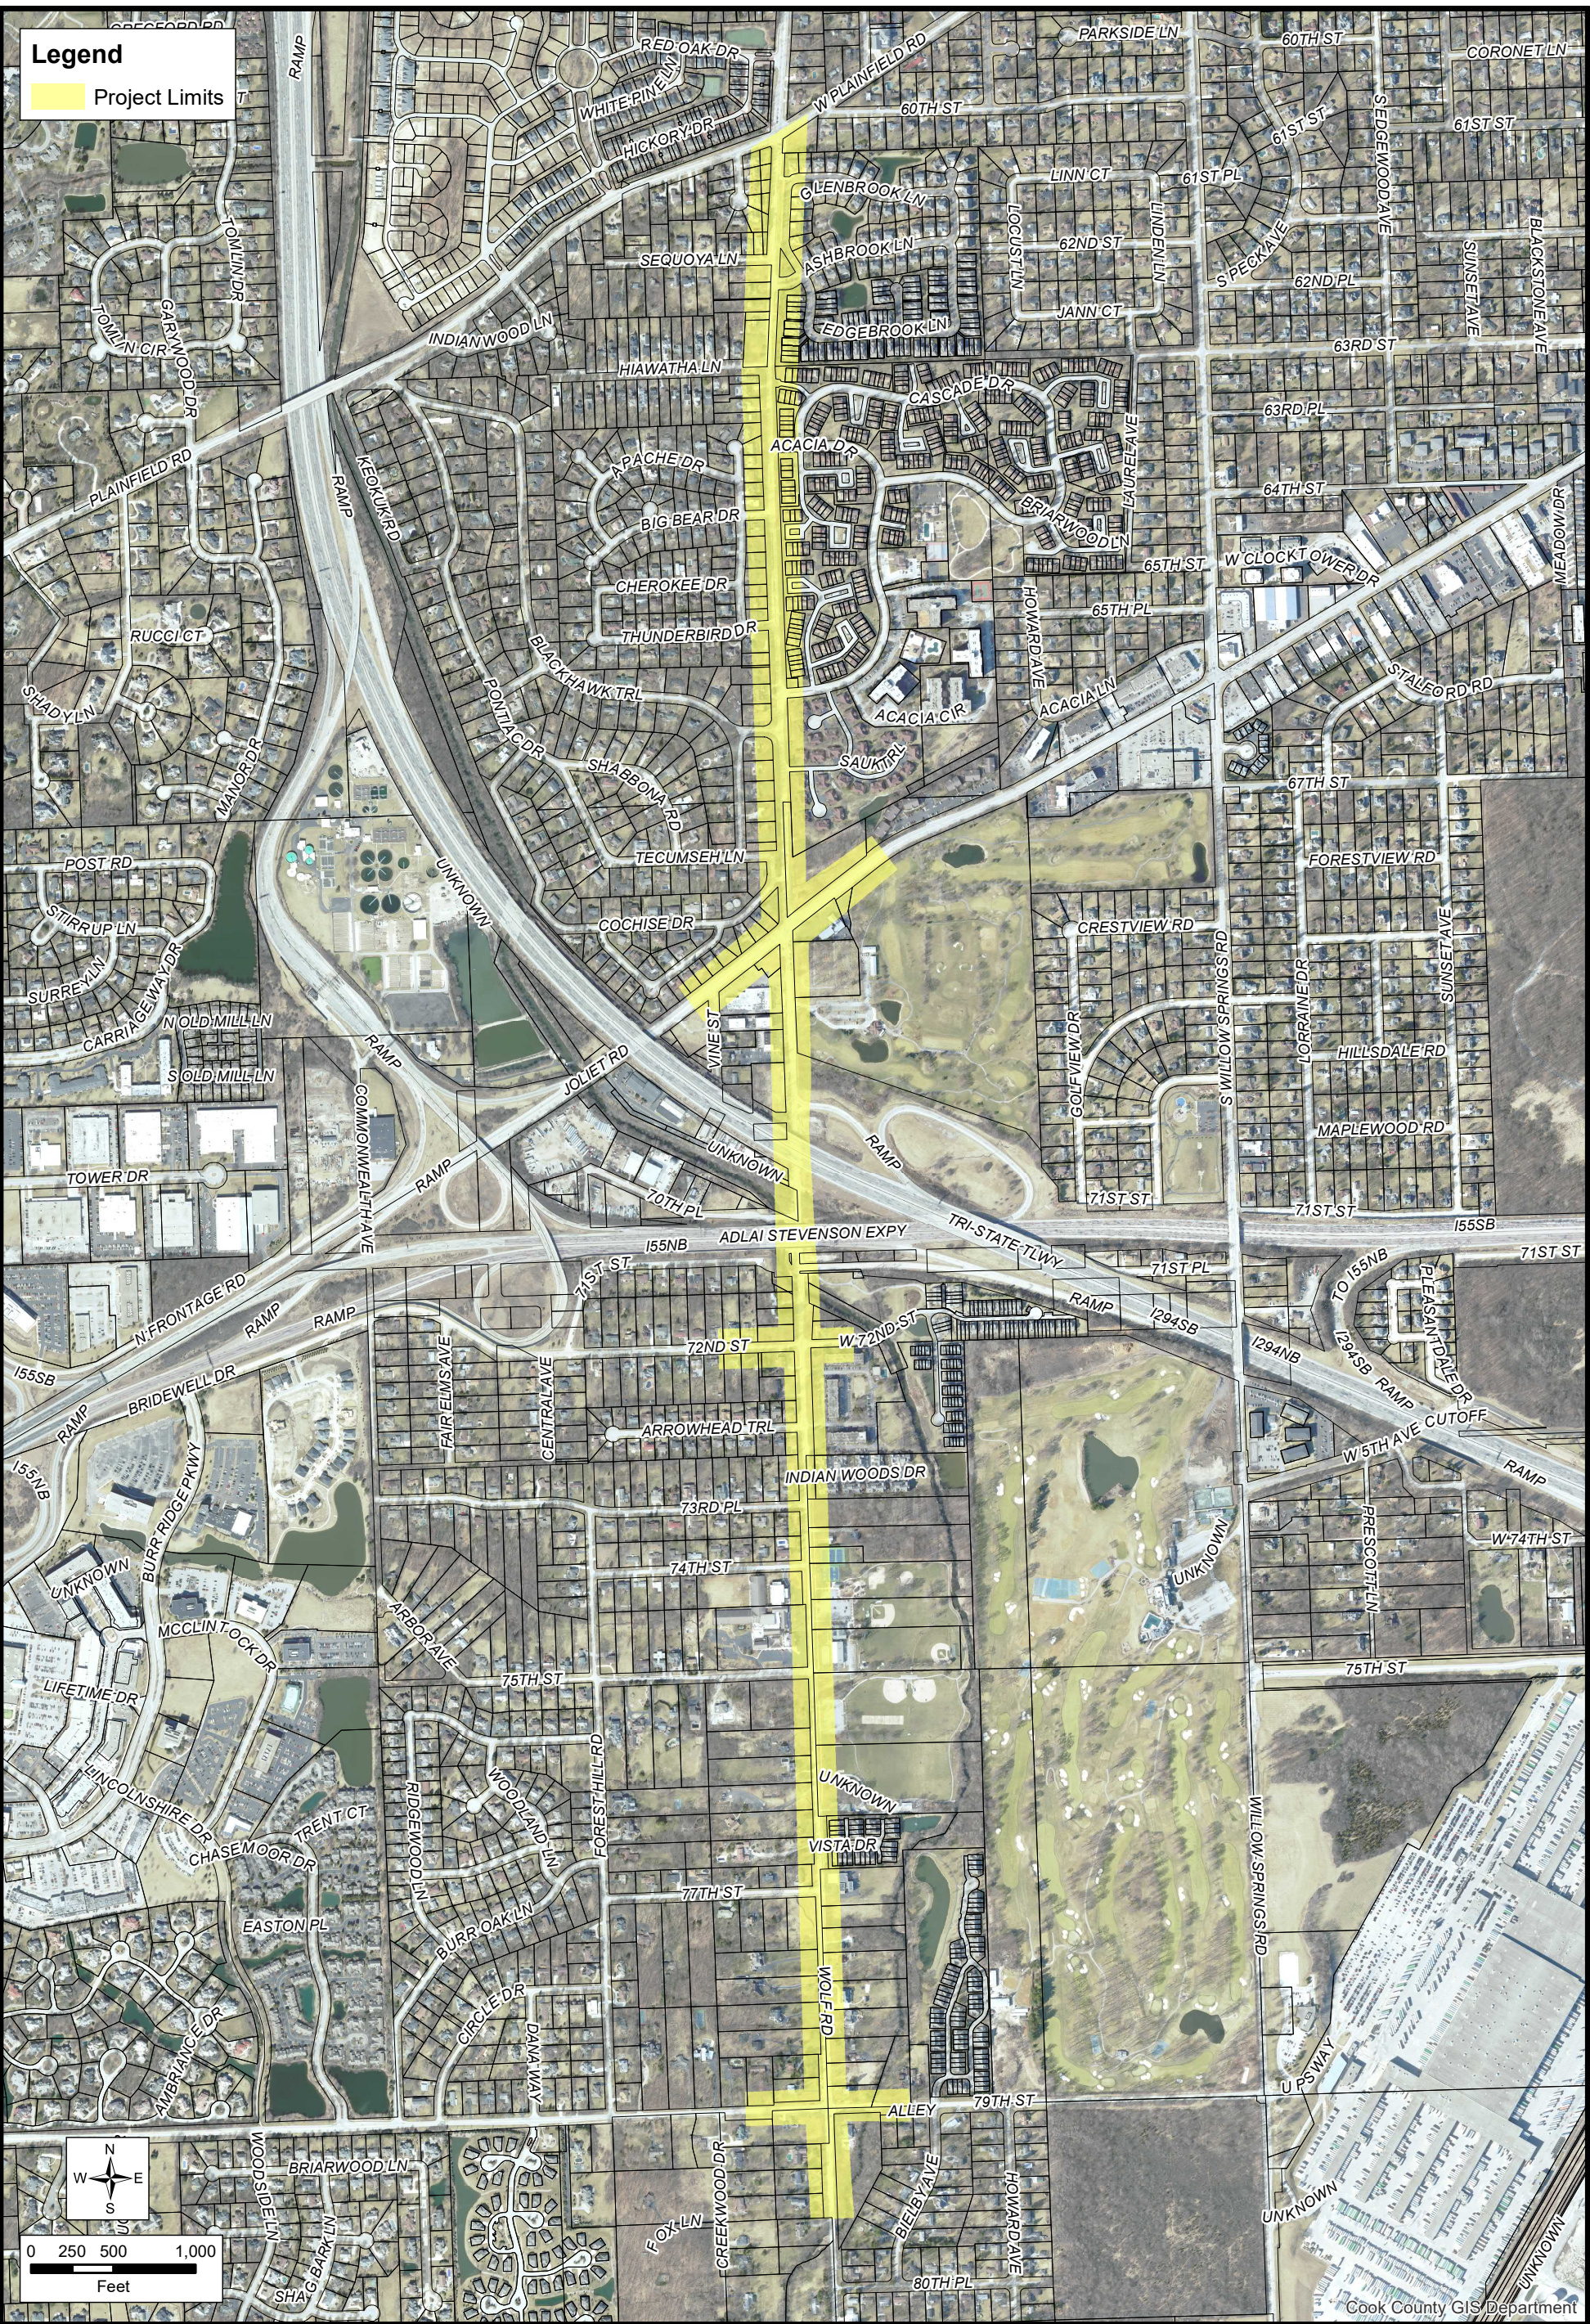

LOCATION MAP

WOLF ROAD RECONSTRUCTION AND WIDENING  
79TH STREET TO PLAINFIELD ROAD  
PHASE I STUDY

VILLAGE OF INDIAN HEAD PARK, ILLINOIS  
SECTION NO. 20-00014-00-PV

**STRAND ASSOCIATES**  
FIGURE 1  
1335.020



**Project Schedule**  
**Wolf Road Reconstruction Phase I**  
**Village of Indian Head Park**  
**Section No. 20-0014-00-PV**

Task	2020			2021												2022														
	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JULY	AUG	SEPT						
<b>1 Data Collection and Evaluation</b>																														
<b>2 Topographical Survey</b>																														
<b>3 Geotechnical Engineering and Analyses</b>																														
<b>4 Environmental Data, Coordination, Inventory, and Analyses</b>																														
Environmental Survey Request			D	R	R	R	R	R	R	R	R	R	R	R	R	A														
Wetland Delineation and Report			D	R	R	R	R	R	R	R	F	R	R	A																
Preliminary Environmental Site Assessment				D	R	R	F	R	R	A																				
Wetland Impact Evaluation											D	R	R	R	R	R	R	R	F	R	R	A								
Tree Survey, Tabulation, and Report														D	R	R	F	R	R	A										
<b>5 Field Evaluation, Structure Condition Assessment, and Condition Reports</b>																														
Field Evaluation and Structure Condition Assessments																														
Bridge Condition Reports, Abbreviated Bridge Condition Reports, and Wall Feasibility Reports				D	R	R	R	F	R	R	A																			
<b>6 Type, Size, and Location Deliverables and Structure Drawings</b>																D	R	R	R	R	R	F	R	R	A					
<b>7 Location Drainage Study</b>																														
Source Data Collection																														
Existing Drainage Plan																														
Proposed Drainage Plan																														
Location Drainage Study																						D	R	R	R	R	F	R	R	A
<b>8 Hydraulic Reports</b>																														
FEMA Regulatory Model and Other Source Data Collection																														
Existing Conditions Analyses					D	R	R	R	R	A																				
Proposed Conditions Analyses																														
Hydraulic Reports																D	R	R	R	R	R	R	F	R	R	A				
<b>9 Hydraulic Coordination and Permitting</b>																														
<b>10 Geometric Studies</b>																														
General Corridor Geometry Tasks																														
Traffic Counts and Data Processing																														
Traffic Projection Coordination with CMAP																														
Traffic Modeling and Capacity Analyses						D	R	R	F	R	R	A																		
Preferred Roadway Alternative Determination																														
Intersection Design Studies																														
<b>11 Crash and Operations Analysis</b>																														
Collect Crash Data for 2016 - 2020 and Prepare Technical Memorandum							D	R	R																					
Update Technical Memorandum with Additional Data from 2021																														
<b>12 Public Involvement</b>																														
Create Stakeholder List, Send Public Initiation Letters, and Log Responses																														
Public Information Meetings																														
<b>13 Section 4(f) Evaluation</b>																														
Evaluate Potential Impacts to 4(f) Properties																														
Prepare and Submit 4(f) Reports																														
<b>14 Meetings</b>																														
CCDOTH / IDOT Kick-Off Meetings																														
Agency Meetings (CCDOTH, IDOT, MWRD, ISTHA, Indian Head Park, Burr Ridge, Willow Springs, IDNR-OWR) as Necessary																														
FHWA Coordination Meetings																														
<b>15 Prefinal Project Development Report - BLR 22210</b>																														
<b>16 Final Project Development Report - BLR 22210</b>																														
<b>17 Administration</b>																														
<b>18 QA/QC</b>																														

<b>LEGEND</b>
D = Draft Submittal
R = Agency Review
F = Final Submittal
A = Anticipated Approval
